

7/26/13

Maynard Conservation Commission  
Maynard Town Hall  
195 Main Street  
Maynard, MA 01754

Re: Weekly Erosion Control Report (Weeks 14-15)  
129 Parker Street, Maynard, MA

Dear Maynard Conservation Commission:

Goddard Consulting, LLC is pleased to submit this site inspection and erosion control report on behalf of Capital Group Properties in accordance with the approved SWPPP (EPA Tracking MAR12AI87) and the Maynard Stormwater Bylaw Permit.

**SITE VISITS:** Goddard has visited and inspected the site on 7/16/13, 7/18/13, 7/23/13, and 7/26/13 in the course of routine site inspections and/or after measurable storm events. There has been a weather pattern of regular light to heavy rain events for the past several weeks. During these recent rain events no erosion occurred in the downgradient receiving stream. The measures outlined in the SWPPP have been implemented including the riser pipes at select catch basins. Goddard believes the site is in reasonable compliance with the SWPPP. It should be noted that some field modifications to the SWPPP have been implemented, namely the centralized basins have been replaced with perimeter trenches. These trenches have proven very effective and have never exceeded their capacity. See attached sketch.

**GENERAL SITE ACTIVITIES:** Another post-demolition sweep is scheduled.

**EROSION SPECIFIC ACTIVITIES:** The following activities were performed:

- All catch basin edges likely to be hit by traffic were sprayed with orange color surveying paint to alert traffic from tearing up fabric.

**IMMEDIATE ACTION ITEMS NEEDED:**

- None.

**LONG-TERM ACTION ITEMS NEEDED:**

- Parking lot shall be inspected and swept quarterly or as needed post demolition given no traffic is expected at the property.

If there are any questions concerning this submission, please do not hesitate to contact us.

Sincerely,  
Goddard Consulting, LLC


by



Scott G Goddard, PWS  
Professional Wetland Scientist

Distribution List via email:

- William Depietri, Capital Group Properties, LLC ([wdepietri@me.com](mailto:wdepietri@me.com))
- Todd Lyons, JBJ Construction ([tlyons@bjcc.net](mailto:tlyons@bjcc.net))

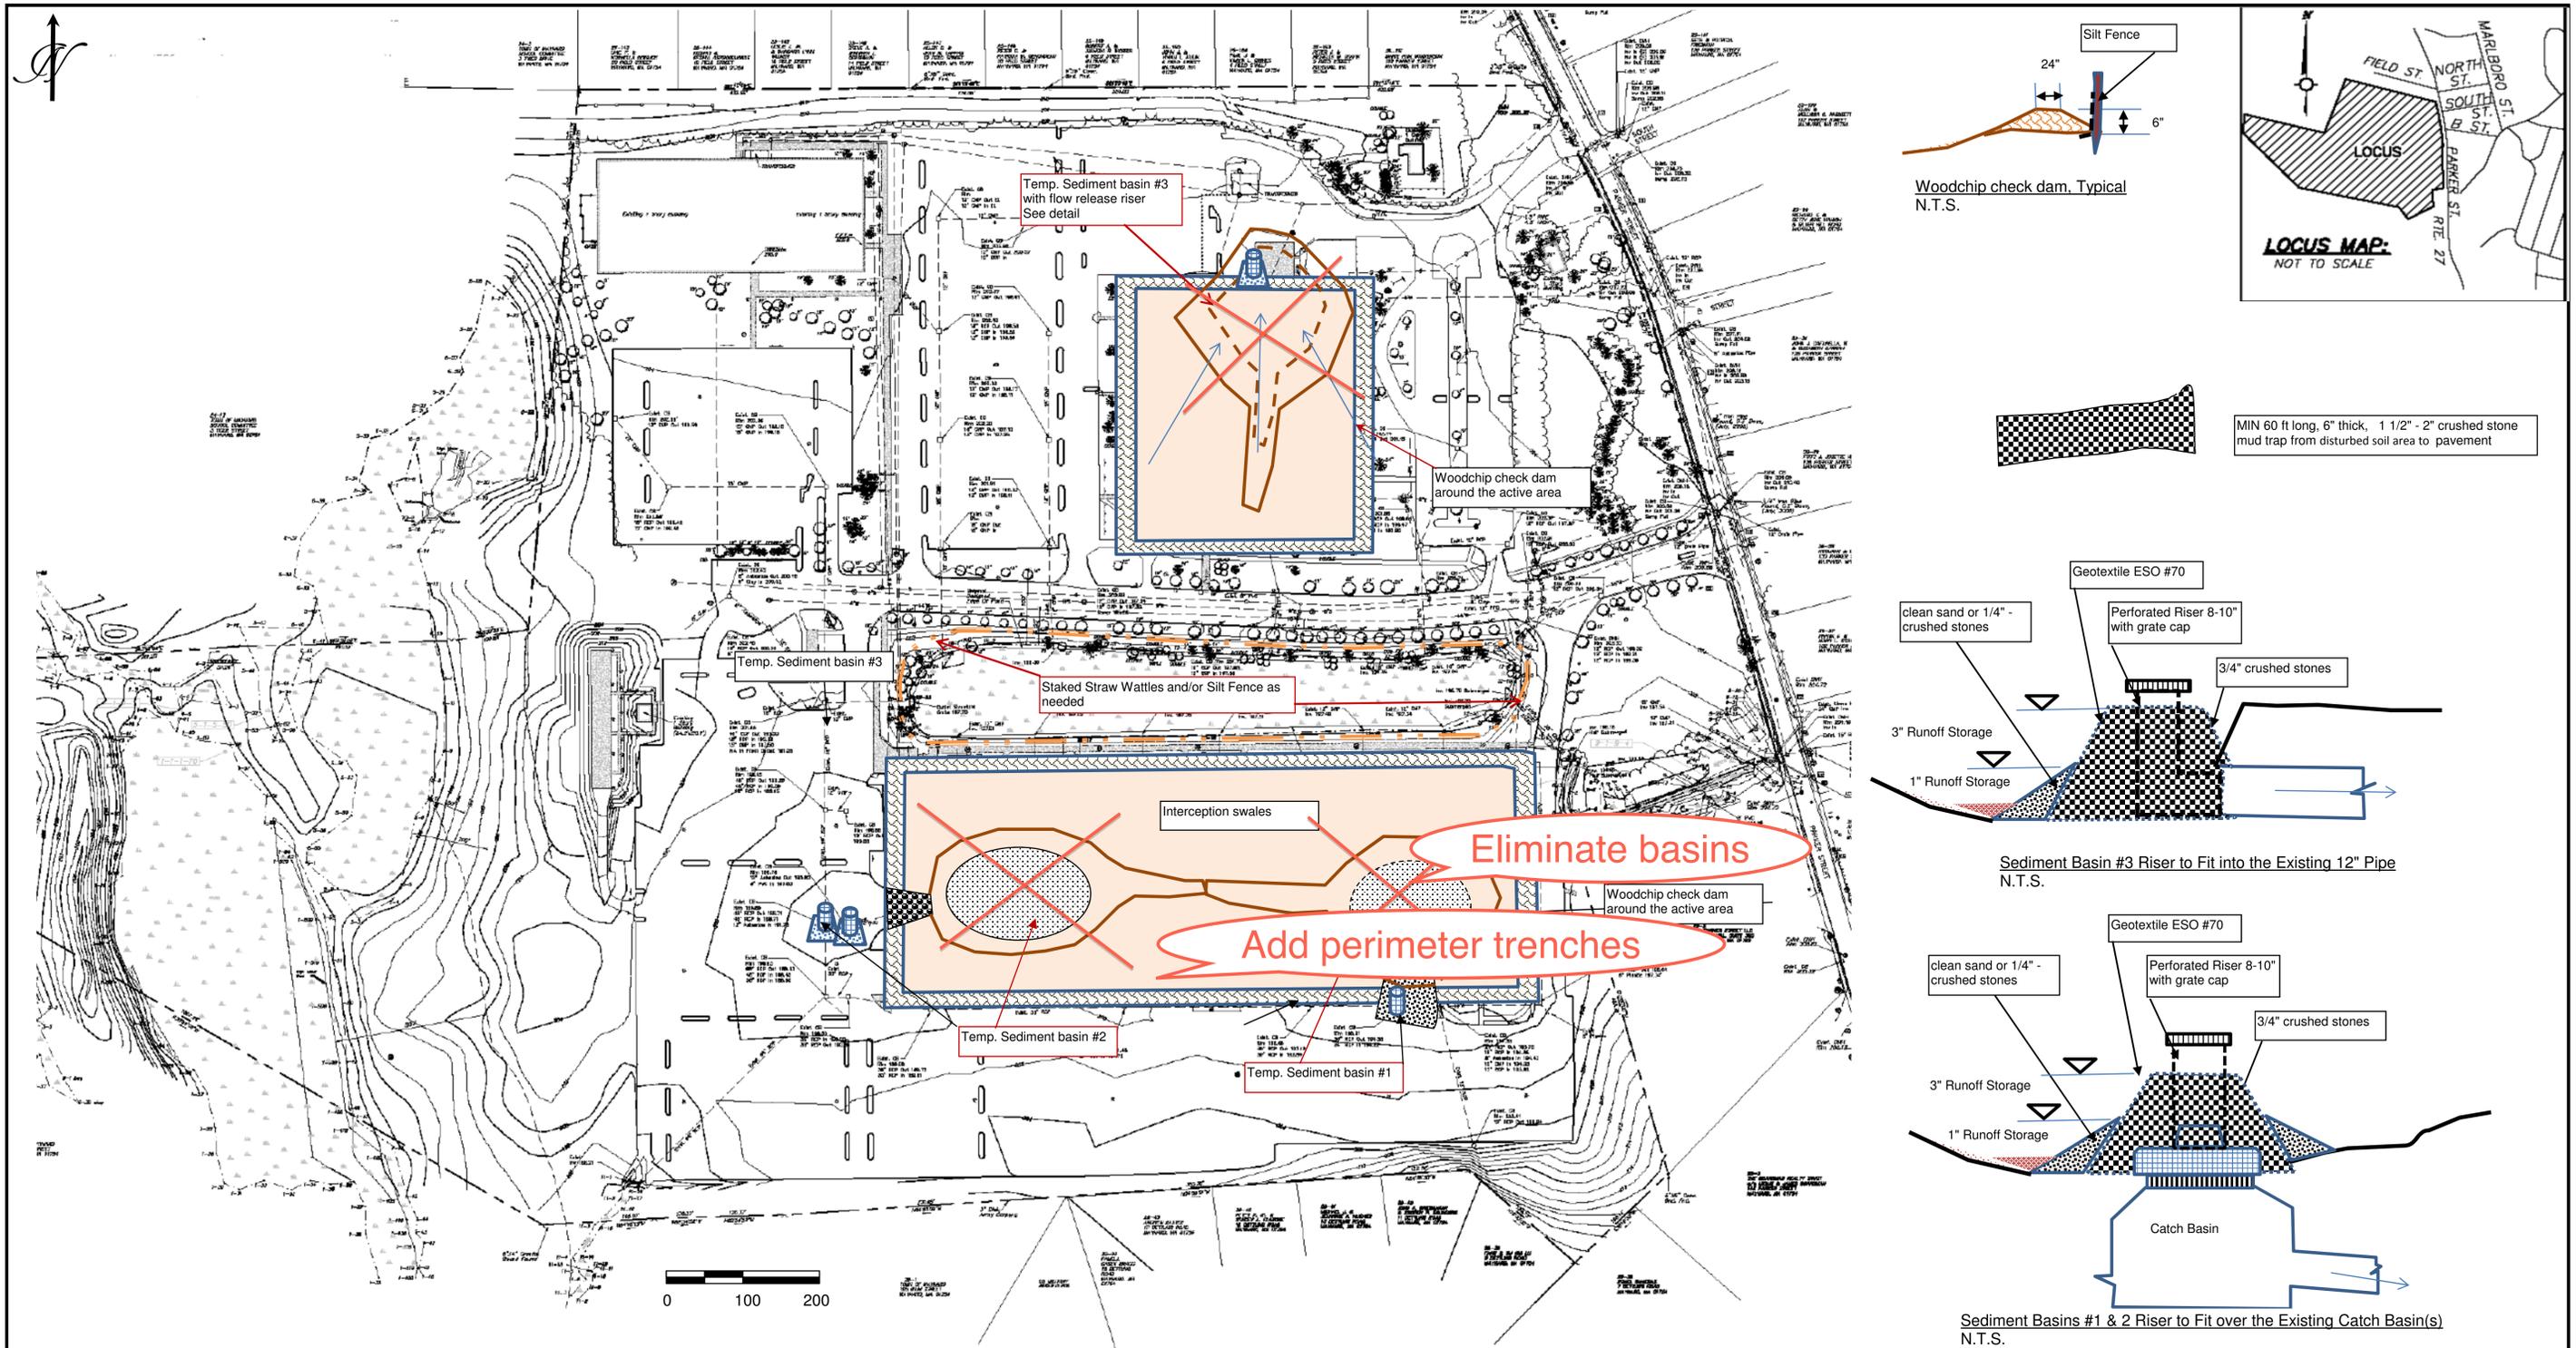

- General Notes:
1. Base map and elevations per "Record Conditions Plan" compiled by Meridian Associates, Westborough, MA, dated May 8, 2009.
  2. Owner/Operator of the Site: William Depietri, Capital Group Properties, LLC, 259 Turnpike Road, Suite 100, Southborough, MA 01772, 508-229-1810 Direct Dial, 508-357-6859 Fax, wdepietri@me.com.
  3. Site lead contractor: Todd Lyons, JBJ Construction, LLC, 259 Turnpike Road, Suite 100, Southborough, MA 01772, 508-400-4260 Cell, tlyons@jbjcc.net
  4. Site Environmental Monitor: Scott Goddard, Goddard Consulting, LLC, 14 Wilson Road, Northborough, MA 01532, scott@goddardconsultingllc.com, (508) 525-0726
  5. A pre-construction meeting is mandatory among the owner, contractor, and the design engineer for construction and future Monitoring.
  6. Bi-weekly and post rainstorm (>0.25") site inspection shall be conducted as planned in the SWPPP for all listed areas of concern and sediment control devices.
  7. All temporarily disturbed soil left for more than 21 days shall be protected with woodchip mulch of 3" +/- thickness.
  8. In addition to what shown in the plan, any outfall or concentrated flow paths identified in the field to wetlands shall be protected with crushed stone check dam or riprap and/or combined with underlying geotextile.
  9. If flocculent or coagulant chemicals are necessary to control turbidity, the design engineer shall be contacted for implementation.

Note: This document has been prepared by Creative Land & Water Engineering, LLC which holds a copy right therein. Coping of any substantial portion of a copyright work without the permission of the copyright owner is unlawful.

	PROJECT TITLE:	Shope's 129 Parker Street, Maynard, MA		<b>Creative Land &amp; Water Engineering, LLC</b> P.O. Box 584 Southborough, MA 01772 774-454-0266 deshengw@yahoo.com
	SHEET TITLE:	Sediment & Erosion Control Plan		
REVISION	NOTES	DESIGNED BY: dsw	APPROVED BY: DSW	
	4/15/2013 Mulch area	DRAWN BY: dsw	DATE: 3/23/2013	
		PROJECT NO.: J174-1	SHEET NO.:	
		SCALE:	As Noted	
